

# SBE and RPP Participation Quarterly Performance Report through March 31, 2022

# THE COMMUNITY — WITHIN THE CORRIDOR



**Submitted by:** 




Date: April 19, 2022

### **Project Summary**

The Community Within the Corridor involves the renovation of several existing buildings on North 33rd Street between Center Street and Hadley Avenue. The buildings will be converted into 64 Corridor Lofts, 36 Crème City Lofts, six 30 Square Townhomes and 91 Briggs Apartment Homes. The development will include a Community Service Facility with early childhood education, Science, Technology, Engineering, Art and Math after-school programming, a health club, laundromat, and a petite grocery store


Developer
Project Address
Construction Manager
Professional Services Cost Subject to Inclusion
Professional Services Draws to Date
Construction Cost Subject to Inclusion
Construction Draws to Date

Community within the Corridor LP
3100 W Center St, Milwaukee, WI 53210
Greenfire Management Services, Inc.
\$2,116,271
\$1,378,688
\$37,540,002
\$21.641.631

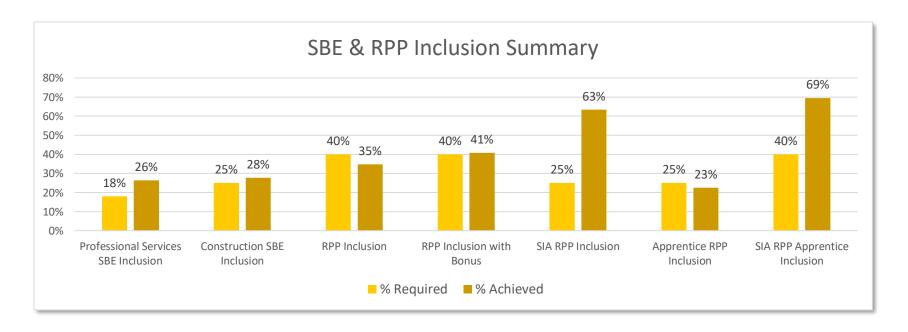

### **SBE Professional Services Inclusion**

Through March 31, 2022, this project has achieved 26% Professional Services inclusion.




Total Value of SBE Payments	Goal/Requirement	Actual	Status
SBE Participation Percentage	18.0%	26%	+8%
Value of SBE Participation	\$380,929	\$556,769	+\$175,840

Table 1: Professional Services Inclusion

			SERVICE PERFORMED OR	SUBCONTRACT	TOTAL AMOUNT
NAME OF CERTIFIED FIRM	DBE/SBE	SUBCONTRACTOR OF	MATERIALS SUPPLIED	AWARD AMOUNT	PAID TO DATE
Cross Management Services, Inc.	SBE	Community wthin the Corridor LP	Inclusion Consultant - Outreach	\$ 22,538	\$ 22,538
Cross Management Services, Inc.	SBE	Greenfire Management Services, Inc.	Inclusion Consultant - Construction	\$ 92,000	\$ 60,000
Jahnke & Jahnke Associates LLC	DBE	Community wthin the Corridor LP	Survey	\$ 24,112	\$ 24,112
K Singh & Associates, Inc.	SBE	Community wthin the Corridor LP	Environmental	\$ 397,599	\$ 397,599
K Singh & Associates, Inc.	SBE	Greenfire Management Services, Inc.	Material Testing	\$ 20,520	\$ 19,166
TOTAL INCLUSION				\$ 556,769	\$ 523,415
INCLUSION, AS PERCENT OF PROFESSIONAL SERVICES COST SUBJECT TO INCLUSION 26%					
INCLUSION, AS PERCENT OF PROF	ESSIONAL	SERVICES DRAW TO DATE			38%

# **SBE Construction Inclusion**

Through March 31, 2022, this project has achieved 28% SBE participation for Construction.



Total Value of SBE Payments	Goal/Requirement	Actual	Status
SBE Participation Percentage	25.0%	28%	+3%
Value of SBE Participation	\$9,385,001	\$10,405,690	+\$1,020,689

Table 2: Construction SBE Inclusion

	DBE/		SERVICE PERFORMED OR	SU	BCONTRACT	то	TAL AMOUNT
NAME OF CERTIFIED FIRM	SBE	SUBCONTRACTOR OF	MATERIALS SUPPLIED	AW	ARD AMOUNT	P.	AID TO DATE
B & D Contractors Inc.	SBE	Greenfire Management Services	Historic Windows	\$	4,991,976	\$	2,599,774
JCP Construction LLC	SBE	Titan Building Company	Rough Carpentry	\$	365,996	\$	174,016
JCP Construction LLC	SBE	Greenfire Management Services	Rough Carpentry	\$	248,019	\$	-
P.L. Freeman Co.	SBE	Greenfire Management Services	HVAC	\$	2,716,792	\$	567,938
RAMS Contracting LTD	SBE	Roofed Right America LLC	Dumpsters	\$	62,659	\$	62,659
Thomas A Mason Company Inc.	SBE	Greenfire Management Services	Painting	\$	1,398,673	\$	458,687
White Glove Group Inc.	SBE	Greenfire Management Services	Asbestos	\$	621,575	\$	519,507
TOTAL INCLUSION				\$	10,405,690	\$	4,382,581
INCLUSION, AS PERCENT OF CONSTRUCTION COST SUBJECT TO INCLUSION 28%							
INCLUSION, AS PERCENT OF COM	INCLUSION, AS PERCENT OF CONSTRUCTION DRAW TO DATE						20%

# **RPP Inclusion**

As shown in the Table 3 below, the RPP inclusion achieved is 35% and increases to 41% when the bonus hours for SIA RPP and Apprentice RPP are included.

**Table 3: RPP Participation by Contractor** 

rable 5. KFF Farticipation by Contra			On-Site	Constructi	on Hours	
Contractor	Trade	Total Hours	RPP	RPP %	SIA RPP	SIA RPP %
		Worked	Worker		Hours	
AGM Erecting LLC	Ironworkers	2,041.00	644.00	32%	644.00	100%
Alpine Insulation 1 LLC	Laborers	3,935.29				
Applewood Drywall	Drywall Finishers	3,473.30				
B&D Contractors, Inc.	Glaziers	6,477.50	1,314.50	20%	710.00	54%
Blair Fire Protection, LLC	Fire Sprinkler Fitters	2,700.50				
Concrete & Masonry Restoration, LLC	Laborers	708.50	264.75	37%	264.75	100%
Harringan Solutions LLC	Laborers	3,281.00	320.00	10%		
Henry R. Marohi, Inc.	Heavy Equipment Operators	3,685.75	1,014.50	28%	981.50	97%
Horner Plumbing	Plumbers	8,310.75	999.00	12%	871.00	87%
Integrity Environmental Service	Laborers	19,844.00	13,510.50	68%	12,740.00	94%
JCP Construction LLC	Carpenters	3,987.50	3,072.00	77%	579.00	19%
KMI Construction, LLC	Bricklayers	16,780.50	3,598.00	21%	2,051.50	57%
L&A Crystal	Terrazzo Finishers	882.04				
Marriott Construction, Inc.	Cement Finishers	3,280.00	78.00	2%	78.00	100%
Midwest Drilled Foundation	Piledrivers	839.50	113.50	14%	113.50	100%
Mindful StaffingSolutions LLC	Roofers	6,150.16	6,150.16	100%	1,656.84	27%
NSI Electrical Contractors, Inc.	Electricians	11,980.25				
P.L. Freeman	Sheet Metal Workers	5,022.00	1,963.00	39%	797.00	41%
Roofed Right America, LLC	Roofers	6,507.53	389.93	6%	389.93	100%
Stanley Harris Trucking	Truck Drivers	850.50	850.50	100%	95.00	11%
Thomas A. Mason Co., Inc.	Painters	3,789.00	1,798.50	47%	423.00	24%
Titan Builidng Company	Carpenters	4,061.00	1,345.50	33%		
Trim Specialists, Inc.	Carpenters	2,348.67	517.25	22%	290.75	56%
Wenger Construction Inc.	Roofers	5,370.75				
White Glove Groups, Inc.	Laborers	12,160.00	10,251.25	84%	7,878.25	77%
Subtotal		138,466.99	48,194.84	35%	30,564.02	63%
Bonus SIA RPP Hours			8,358.66			
Total RPP Hours		138,466.99	56,553.50	41%		

Table 4: RPP Participation by Craft

		# of RPP
Craft	RPP Hours	Workers
Acoustic Ceilng Installer	38.00	1
Bricklayers	3,060.00	6
Carpenters	4,358.25	7
Cement Finishers	78.00	1
Glaziers	710.00	1
Ironworkers	644.00	1
Laborers	30,457.76	91
Painters	1,760.50	6
Piledrivers	113.50	2
Plumbers	935.00	3
Roofers	3,002.33	11
Sheet Metal Workers	1,931.00	4
Truck Drivers	850.50	2
Tuckpointers	256.00	2
Total	48,194.84	138

Table 6: RPP Participation by Race

		# of RPP
Race	RPP Hours	Workers
African-American	16,055.46	46
Asian	1,033.50	2
Causasian	3,319.10	13
Hispanic	23,289.65	64
Native American	710.00	1
Not Specified	3,787.13	12
Total	48,194.84	138

Table 5: RPP Participation by Zip Code

		# of RPP
Zip Code	RPP Hours	Workers
53202	1,004.93	2
53204	8,670.50	24
53205	160.00	1
53206	162.25	2
53207	565.00	3
53208	2,342.85	7
53209	2,873.80	6
53210	3,083.57	7
53211	182.50	2
53212	1,387.17	5
53214	1,232.50	3
53215	14,757.68	43
53216	5,973.36	12
53218	1,291.18	6
53219	613.14	3
53220	691.50	2
53221	229.50	1
53222	1,007.50	2
53223	669.50	3
53225	1,296.41	4
Total	48,194.84	138

**Table 7: RPP Participation by Gender** 

Gender	RPP Hours	# of RPP Workers
Male	48,130.34	137
Female	64.50	1
Not Specified		
Total	48,194.84	138

Table 8: Apprenticeship & On-The-Job Trainee Participation

	# of	Total	RPP	RPP	SIA RPP	SIA RPP
	Apprentices /	Hours	Apprentice	<b>Apprentice</b>	Apprentice	Apprentice
Craft	OJT Trainees	Worked	Hours	%	Hours	%
Acoustic Ceiling Installer	1	38.00	38.00	100%	38.00	100%
Bricklayers	6	1,915.00	1,244.00	65%	784.50	63%
Carpenters	4	857.45	537.50	63%	537.50	100%
Electricians	13	4,645.00				
Fire Sprinkler Fitters	7	733.00				
Glaziers	2	926.50				
Heavy Equipment Operators	2	146.00				
Ironworkers	2	415.00				
Laborers	6	2,071.50	576.50	28%		
Painters	4	705.50	306.50	43%	203.50	66%
Piledrivers	1	75.00	75.00	100%	75.00	100%
Plumbers	15	2,831.00	807.00	29%	807.00	100%
Roofers	17	2,822.50				
Sheet Metal Workers	6	2,525.50	1,081.00	43%	797.00	74%
Total	86	20,706.95	4,665.50	23%	3,242.50	69%

**Table 9: Apprentice Participation by Race** 

Race	Hours	# of Workers
African-American	2,582.00	9
Asian	1,078.25	2
Causasian	8,864.25	38
Hispanic	893.45	7
Native American		
Not Specified	7,289.00	30
Total	20,706.95	86

**Table 10: Apprentice Participation by Gender** 

Gender	Total Hours	# of Workers
Male	20,706.95	86
Female		
Not Specified		
Total	20,706.95	86
