
MILWAUKEE SYMPHONY ORCHESTRA

2nd Street Public Infrastructure

SBE and RPP Participation Quarterly Performance Report through September 30, 2020



Submitted by:

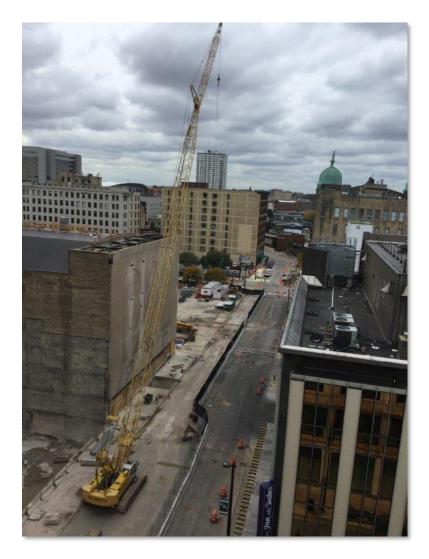

Date: November 11, 2020 - Corrected


Project Summary

North 2nd Street between West Wisconsin and West Wells Avenues is being reconstructed to compliment The Grand Theater, the new home for the Milwaukee Symphony Center. This project is undertaken by the City of Milwaukee, Redevelopment Authority of the City of Milwaukee and TNSH Landlord LLC.

| Developer | TNSH Landlord LLC |
|---|---|
| Project Address | 200 – 208 and 212 West Wisconsin Avenue, WI 53203 |
| Construction Manager | C. D. Smith Construction |
| Professional Services Cost Subject to Inclusion | \$60,869 |
| Professional Services Draws to Date | \$54,857 |
| Construction Cost Subject to Inclusion | \$1,936,155 |
| Construction Draws to Date | \$1,006,512 |

SBE Professional Services Inclusion

Through September 30, 2020, this project has achieved 19.7% Professional Services inclusion.



SBE Goal/Requirement

SBE Actual


| Total Value of SBE Payments | Goal/Requirement | Actual | Status |
|------------------------------|------------------|----------|----------|
| SBE Participation Percentage | 18.0% | 19.7% | +1.7% |
| Value of SBE Participation | \$10,956 | \$12,000 | +\$1,044 |

Table 1: Professional Services Inclusion

| NAME OF CERTIFIED FIRM | SBE | SUBCONTRACTOR OF | SERVICE PERFORMED OR MATERIALS SUPPLIED | CONTRACT | | L AMOUNT TO DATE |
|--|-----|--------------------------------------|--|--------------|-------|---------------------|
| Cross Management Services, Inc. | SBE | Milwaukee Symphony Orchestra (M S O) | Inclusion Consultant | \$ 12,000 | \$ | 8,988 |
| TOTAL INCLUSION | | | | \$ 12,000 | \$ | 8,988 |
| INCLUSION, AS PERCENT OF PROFESSIONAL SERVICES COST SUBJECT TO INCLUSION | | | | 19.7% | | |
| INCLUSION, AS PERCENT OF PROFESSIONAL SERVICES DRAWS | | | | 1 | 16.4% | |

SBE Construction Inclusion

Through September 30, 2020, this project has achieved 26.7% SBE participation for Construction.



SBE Goal/Requirement

SBE Actual

| Total Value of SBE Payments | Goal/Requirement | Actual | Status |
|------------------------------|------------------|-----------|-----------|
| SBE Participation Percentage | 25.0% | 26.7% | +1.7% |
| Value of SBE Participation | \$484,039 | \$516,578 | +\$32,539 |

Table 2: Construction SBE Inclusion

| | | | SERVICE PERFORMED OR | SU | BCONTRACT | TOT | AL AMOUNT | RE | MAINING |
|------------------------------------|-----------|---------------------------|--------------------------|----|------------|------|-----------|----|---------|
| NAME OF CERTIFIED FIRM | SBE | SUBCONTRACTOR OF | MATERIALS SUPPLIED | AW | ARD AMOUNT | PAID | TO DATE | BA | LANCE |
| Construction Services of Milwaukee | SBE | Michels Foundations | Concrete Labor | \$ | 150,000 | \$ | - | \$ | 150,000 |
| Dedicated Contractors | SBE | CD SMITH Construction | City Underground Conduit | \$ | 189,999 | \$ | 170,999 | \$ | 19,000 |
| Hawk Industries | DBE | CD SMITH Construction | Concrete Support - Alley | \$ | 40,863 | \$ | - | \$ | 40,863 |
| RB General Trucking | SBE | MJ Construction, Inc. | Trucking | \$ | 95,866 | \$ | 95,866 | \$ | • |
| Security Officer Services | SBE | CD SMITH Construction | Security | \$ | 38,000 | \$ | 11,659 | \$ | 26,341 |
| WI Utility Exposure | SBE | MJ Construction, Inc. | Hydro-Excavation | \$ | 1,850 | \$ | 1,850 | \$ | • |
| TOTAL INCLUSION | | | | \$ | 516,578 | \$ | 280,375 | \$ | 236,204 |
| INCLUSION, AS PERCENT OF CONST | RUCTION (| COST SUBJECT TO INCLUSION | | | 26.7% | | | | |
| INCLUSION, AS PERCENT OF CONST | RUCTION D | DRAWS | | | | | 27.9% | | |

RPP Participation¹

As shown in the Table 3 below, the RPP inclusion achieved is 59.5% when the bonus hours for SIA RPP and RPP Apprentice hours are included. The SIA RPP bonus hours and Apprentice RPP bonus hours were calculated in accordance with the following Sections of the HR Agreement for the project:

Section III.A.2. of the HR Agreement reads,

"In accordance with sec. 355-7-2-a-1 of the MCO, at least one-quarter of the 40% resident utilization requirement shall be performed by unemployed or underemployed residents who maintain their permanent residence in zip codes established as high-poverty. Every worker hour exceeding this requirement shall count for **1.5** hours toward the overall 40% resident utilization requirement for the PROJECT." (bold added)

| Bonus SIA RPP Hours | 615.00 |
|------------------------|--------|
| Excess SIA RPP Hours | 410.00 |
| Required SIA RPP Hours | 315.00 |
| Actual SIA RPP Hours | 725.00 |

Section III.E.1 of the HR Agreement reads,

"One-quarter of the apprentices and on-the-job trainees required for the PROJECT as measured in worker hours, shall be unemployed or underemployed residents of the CITY. For every worker hour exceeding the requirements of this subsection, **1.5** hours shall be credited toward the 40% resident utilization requirement for the PROJECT." (bold added)

| Bonus Apprentice RPP Hours | 62.44 |
|-------------------------------|--------|
| | |
| Excess RPP Apprentice Hours | 41.63 |
| Required RPP Apprentice Hours | 79.88 |
| Actual RPP Apprentice Hours | 121.50 |

¹ Tables 3 – 10 were prepared using a LCPtracker report generated on 10/22/2020 for the period of 1/1/2015 through 9/30/2020.

Table 3: RPP Participation by Contractor

| RPP Report | | | | | | | |
|--|------------------|----------------------------|----------|--------|---------|-----------|--|
| | | On-Site Construction Hours | | | | | |
| Contractor | Trade | Total | RPP | RPP % | SIA RPP | SIA RPP % | |
| | | Hours | Worker | RFF 70 | Hours | SIA RFF % | |
| C.D. Smith | Concrete | 122.50 | | | | | |
| Construction Services of Milwaukee LLC | Cement Finishing | 119.00 | | | | | |
| MJ Construction Inc. | Excavation | 1,813.00 | 610.50 | 33.7% | 139.50 | 22.9% | |
| Michels Corporation | Cement Finishing | 155.50 | | | | | |
| SOS Security Officer Services, Inc. | Security | 666.50 | 312.00 | 46.8% | 312.00 | 100.0% | |
| Szade Trucking Inc. | Trucking | 273.50 | 273.50 | 100.0% | 273.50 | 100.0% | |
| Total Hours | · | 3,150.00 | 1,196.00 | 38.0% | 725.00 | 60.6% | |
| Bonus SIA RPP Hours | | | 615.00 | | | | |
| Bonus Apprentice RPP Hours | | | 62.44 | | | | |
| Total RPP Hours | | 3,150.00 | 1,873.44 | 59.5% | | | |

Table 4: RPP Participation by Craft

| | | # of RPP |
|--------------------------|-----------|----------|
| Craft | RPP Hours | Workers |
| Heavy Equipment Operator | 488.00 | 3 |
| Laborers | 434.50 | 9 |
| Truck Drivers | 273.50 | 3 |
| Total | 1,196.00 | 15 |

Table 5: RPP Participation by Zip Code

| | RPP | # of RPP |
|----------|----------|----------|
| Zip Code | Hours | Workers |
| 53204 | 52.00 | 1 |
| 53206 | 208.00 | 1 |
| 53209 | 52.00 | 1 |
| 53212 | 53.50 | 1 |
| 53215 | 216.75 | 4 |
| 53218 | 68.00 | 2 |
| 53219 | 32.00 | 1 |
| 53220 | 135.00 | 1 |
| 53221 | 234.75 | 2 |
| 53225 | 144.00 | 1 |
| Total | 1,196.00 | 15 |

Table 6: RPP Participation by Race

| | RPP | # of RPP |
|------------------|----------|----------|
| Ethnicity | Hours | Workers |
| African American | 208.00 | 1 |
| Causasian | 909.25 | 12 |
| Hispanic | 78.75 | 2 |
| Total | 1,196.00 | 15 |

Table 7: RPP Participation by Gender

| | RPP | # of RPP |
|--------|----------|----------|
| Gender | Hours | Workers |
| Male | 1,144.00 | 14 |
| Female | 52.00 | 1 |
| Total | 1,196.00 | 15 |

Table 8: Apprenticeship & On-The-Job Trainee Participation

| Apprentice Report | | | | | | | | |
|-------------------|---------------------------------------|--|--------------------------------------|------------------------|---|----------------------------|--|--|
| Craft | # of Apprentices / OJT Trainees | Total Apprentice Hours Worked | RPP Apprentice Worker Hours | RPP Apprentice % | SIA RPP Apprentice Workers Hours | SIA RPP Apprentice % | | |
| Laborers | 4 | 145.50 | 121.50 | 83.5% | 53.50 | 44.0% | | |
| Operators | 1 | 174.00 | | 0.0% | | | | |
| Total | 5 | 319.50 | 121.50 | 38.0% | 53.50 | 44.0% | | |

Table 9: Participation by Race

| | RPP | # of RPP |
|------------------|--------|----------|
| Ethnicity | Hours | Workers |
| African American | | |
| Causasian | 121.50 | 3 |
| Hispanic | | |
| Total | 121.50 | 3 |

Table 10: Participation by Gender

| | RPP | # of RPP |
|--------|--------|----------|
| Gender | Hours | Workers |
| Male | 121.50 | 3 |
| Female | | |
| Total | 121.50 | 3 |

MSO – 2ND STREET INFRASTRUCTURE PROJECT – September 2020 Corrected
