



# KOMATSU

## Mining Corp.

Data through June 30, 2021



Prepared by



TABLE OF CONTENTS

3  
Executive Summary  
History  
Project Team  
Goals


4  
Inclusion  
SBE Professional Services  
SBE Construction  
RPP



Komatsu is building a state-of-the-art manufacturing and global mining campus in Milwaukee's Harbor District. Work on the new campus is expected to create over 2,000 construction jobs. Komatsu expects to invest approximately \$285 million dollars in the project. When complete, it will include engineering and robotics labs, a large office complex, a customer experience center, a modern manufacturing facility and more - with potential to employ more than a thousand people. Construction of the campus is expected to be complete in 2022.

The project's design will be completed by Eppstein Uhen Architects (EUA) and GRAEF, and construction by Construction Manager/General Contractor, Hunzinger Construction Company. Prism Technical Management & Marketing Services, LLC (Prism) has been contracted to assist in the achievement of project inclusion goals: 40% RPP workforce; and contract spend of 25% Construction and 18% Professional Services.

The new Milwaukee campus will allow Komatsu to combine operations from two of its three Milwaukee-area facilities: one off National Avenue in West Milwaukee and the other at the Honey Creek Corporate Center in Wauwatosa.

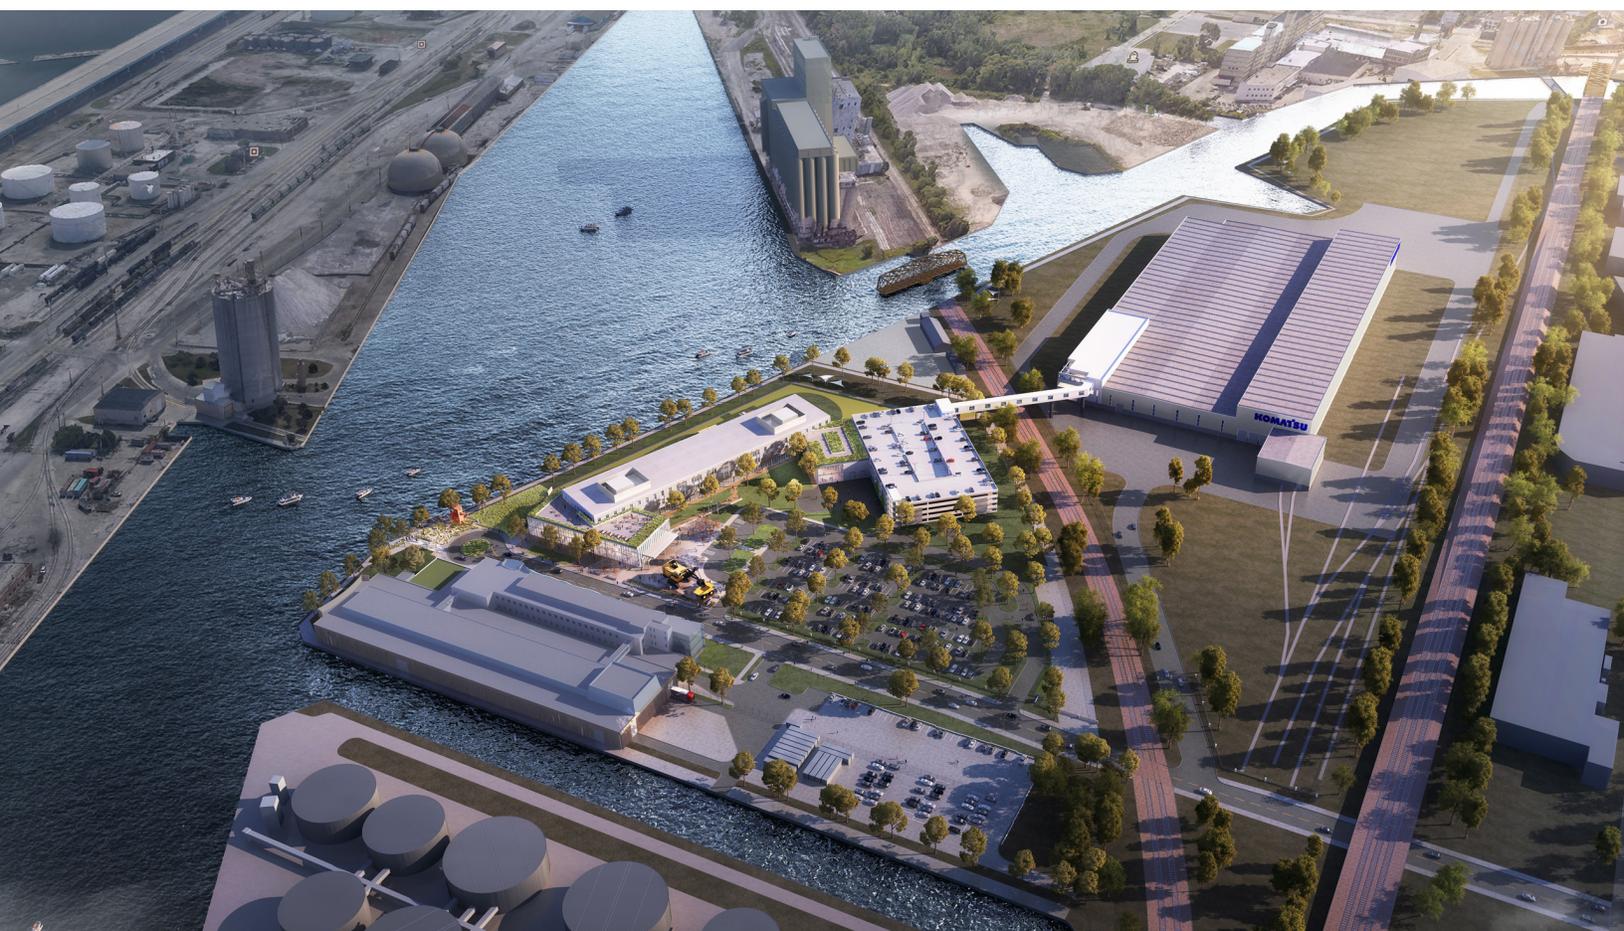

**SBE Participation: Professional Services**

The Total Adjusted budget to date is \$6,862,604 with SBE/DBE firms holding \$1,373,595 in contracts or 20.0%. Professional Service SBE firms were paid \$1,271,446 or 92.6% of their contract value through June 2021.

**TABLE 1: PROFESSIONAL SERVICES CONTRACTS through June 2021**

Firm	Contracted by	Scope of Services	Value Subject to Participation
EUA/Graef	Komatsu	Lead Architectural and Engineering services	\$5,969,498
GESTRA Engineering	Komatsu	Geotechnical /Testing & Environmental Drilling	\$383,995
Avantti Design Group, LLC*	Hunzinger Construction Co.	Pre-Engineered Metal Building Design	\$250,081
Prism Technical Management & Marketing	Komatsu	Inclusion Consultants	\$259,030
<b>TOTAL</b>			<b>\$6,862,604</b>

**TABLE 2: SBE PROFESSIONAL SERVICES INCLUSION through June 2021**

SBE Firm	Contracted by	Scope of Services	Awarded Contract Value	Paid to Date	% of Contract paid through June 2021
Prism Technical Management & Marketing	Komatsu	Inclusion Consultants	\$259,030	\$182,321	70.4%
GESTRA Engineering	Komatsu	Engineering/Testing	\$384,995	\$384,995	100.0%
ADG Avantti Design Group, LLC*	Hunzinger Construction Co.	Pre-Engineered Metal Building Design	\$250,081	\$250,081	100.0%
Bloom Companies, LLC	EUA	Structural Engineering	\$129,440	\$129,440	100.0%
IBC Engineering Services, Inc.	EUA	Mech/Elec/Plumbing Engineering	\$120,475	\$105,416	87.5%
M&E Architects + Engineers, LLC	EUA	Architectural Consulting	\$155,900	\$155,900	100.0%
Stormwater Solutions Engineering, LLC	EUA	Civil Engineering	\$32,874	\$25,331	77.1%
TerraTec Engineering, LLC	EUA	Civil Engineering	\$40,800	\$37,963	93.0%
<b>TOTAL</b>			<b>\$1,373,595</b>	<b>\$1,271,446</b>	<b>92.6%</b>

Project Subject to Participation	
Total Contracts	\$6,862,604
SBE Contract Participation	20.0%
<b>Project Goal is 18%</b>	

## PROFESSIONAL SERVICES SBE INCLUSION

GRAPH 1

### Contract Participation



GRAPH 2

### Payments To Date



Steamfitter installing grill in kitchen.

## SBE Participation: Construction

The Total Adjusted budget to date is \$149,950,702 with SBE/DBE firms holding \$63,410,314 in contracts or 42.3%. Construction Services SBE firms were paid \$39,420,441 or 62.2% of their contract value through June 2021.

TABLE 3: CONSTRUCTION CONTRACT through June 2021

Firm	Contracted by	Scope of Work	Value Subject to Participation
Hunzinger Construction Co.	Komatsu	General Contractor	\$149,950,702

TABLE 4: SBE CONSTRUCTION INCLUSION through June 2021

SBE Firm	Contracted by	Scope of Work	SBE Contract Value	SBE Paid to Date	% of Contract paid through June 2021
Avanti Design Group, LLC (1)	Hunzinger Construction Co.	Pre Engineered Metal Building	\$15,599,838	\$14,395,957	92.3%
Arrow-Crete Construction, LLC	Cornerstone One, LLC	Concrete Work	\$25,000		0.0%
Benavides Construction, Inc.	Cornerstone One, LLC	Subcontractor/Supplier	\$25,000		0.0%
Best Clearcut Solutions, LLC	Hunzinger Construction Co.	Concrete Coring - Machine Bases	\$102,512		0.0%
Best Erectors, Inc.	Midwest Stairs & Iron	Supply/Install Misc. Metals	\$533,516		0.0%
Construction Services of Milwaukee, LLC	Michels Corp.	Onsite Pile Work	\$837,437	\$1,385,283	165.4%
Dairyland Energy Solutions, Inc.	Cornerstone One, LLC	Plumbing Systems - Office	\$754,750	\$91,000	12.1%
Dairyland Energy Solutions, Inc.	Cornerstone One, LLC	Plumbing Material - Manufacturing	\$4,093	\$4,093	100.0%
Dairyland Energy Solutions, Inc.	Staff Electric Co., Inc.	Electrical - Man., Bridge & Site	\$36,470		0.0%
DSR Millwright	Staff Electric Co., Inc.	Stage/Inspect Machinery	\$38,038		0.0%
Duwe Metal Products, Inc.	Superior Masonry	Concrete Slabs	\$1,826,650	\$22,500	1.2%
Duwe Metal Products, Inc.	Hunzinger Construction Co.	Reinforcing Steel - Machine Bases	\$1,631,969	\$466,965	28.6%
Duwe Metal Products, Inc.	Hunzinger Construction Co.	Misc. Metals - Machine Bases	\$1,038,769	\$466,965	45.0%
Duwe Metal Products, Inc.	Hunzinger Construction Co.	Supply/Install Misc. Metals - Office	\$897,420	\$466,965	52.0%
Duwe Metal Products, Inc.	Hunzinger Construction Co.	Reinforcing Steel - Office	\$1,801,790	\$466,965	25.9%
Duwe Metal Products, Inc.	Hunzinger Construction Co.	Reinforcing Steel - Bay 1-4	\$681,609	\$466,965	68.5%
Duwe Metal Products, Inc.	Hunzinger Construction Co.	Reinforcing Steel - Bay 5	\$620,521	\$466,965	75.3%
Duwe Metal Products, Inc.	Hunzinger Construction Co.	Reinforcing Steel - Parking Deck	\$371,276	\$466,965	125.8%
Duwe Metal Products, Inc.	Hunzinger Construction Co.	Reinforcing Steel - Bridge	\$30,831	\$30,831	100.0%
Duwe Metal Products, Inc.	Hunzinger Construction Co.	Reinforcing Steel - Monuments	\$31,738	\$31,738	100.0%
Duwe Metal Products, Inc.	Klein-Dickert Milwaukee, Inc.	Window System	\$1,164,307	\$792,663	68.1%
Duwe Metal Products, Inc.	Staff Electric Co., Inc.	Produce Custom Enclosures	\$12,311		0.0%
EFH Trucking, LLC	Payne & Dolan, Inc.	Trucking - Asphalt	\$9,050		0.0%
Equity Supply Group, LLC	Muza Sheet Metal Co.	Insulation	\$41,366	\$41,366	100.0%
Equity Supply Group, LLC	Muza Sheet Metal Co.	ACM Panel Material	\$124,834	\$124,834	100.0%
Express Insulation, Inc.	Cornerstone One, LLC	Plumbing Systems	\$301,535		0.0%
Gordon Solutions, LLC	Klein-Dickert Milwaukee, Inc.	Labor	\$36,235	\$36,235	100.0%
Hard Rock Sawing & Cutting Co.	Cornerstone One, LLC	Concrete Cutting	\$7,345	\$7,345	100.0%
Heider & Bott Co.	Cornerstone One, LLC	Material Supplier	\$188,072		0.0%
Hetzel-Sanfilippo, Inc.	Hunzinger Construction Co.	Framing & Drywall with Fireproofing	\$4,273,421	\$2,166,241	50.7%
Hiram Power Electric, LLC	Staff Electric Co., Inc.	Fixtures & Lighting	\$2,460,425	\$1,857,041	75.5%
House of Stone, Inc.	Tri Formed Top Corp.	Supply/Install Countertops	\$312,434		0.0%
Hurt Electric, Inc.	Hunzinger Construction Co.	Electrical - Office, Parking Deck & Site	\$4,676,722	\$3,010,618	64.4%

TABLE 4 cont.: SBE CONSTRUCTION INCLUSION through June 2021

SBE Firm	Contracted by	Scope of Work	SBE Contract Value	SBE Paid to Date	% of Contract paid through June 2021
Hurt Electric, Inc.	Pieper Electric, Inc.	Temp Site Electric	\$99,340		0.0%
HVA Products, Inc.	Grunau Co.	HVAC Office & Parking Deck	\$555,870	\$449,644	80.9%
HVA Products, Inc.	Lee Plumbing & Mechanical	HVAC Manufacturing & Bridge	\$421,238		0.0%
JCP Construction, LLC	Hunzinger Construction Co.	Foundation Concrete - Man. Bay	\$576,170	\$518,355	90.0%
JCP Construction, LLC	Hunzinger Construction Co.	Bridge Carpentry	\$54,069		0.0%
JCP Construction, LLC	Hunzinger Construction Co.	Manufacturing & Parking Carpentry	\$289,409		0.0%
JCP Construction, LLC	Hunzinger Construction Co.	Office Carpentry	\$33,930		0.0%
JCP Construction, LLC	Hunzinger Construction Co.	Prime Contractor	\$216,654	\$216,654	100.0%
JCP Construction, LLC	Hunzinger Construction Co.	Foundation Concrete - Office	\$128,500		0.0%
JCP Construction, LLC	Muza Sheet Metal Co.	Exterior Metal Panel System	\$374,407	\$47,365	12.7%
JCP Construction, LLC	Muza Sheet Metal Co.	Jobsite Labor	\$81,513	\$81,513	100.0%
KMI Construction, LLC	Hunzinger Construction Co.	Office Masonry	\$1,393,741	\$408,635	29.3%
Peachy Clean Commercial & Construction Cleaning, LLC	Hunzinger Construction Co.	Construction Cleaning	\$11,790	\$11,790	100.0%
P.J.'s Trucking, LLC	Payne & Dolan, Inc.	Trucking - Asphalt	\$9,050		0.0%
P.L. Freeman Co.	Cornerstone One, LLC	Subcontractor/Supplier - Site Utilities	\$150,014	\$88,259	58.8%
P.L. Freeman Co.	Lee Plumbing & Mechanical	Jobsite Labor & Equipment	\$2,126,803	\$730,489	34.3%
P.L. Freeman Co.	MM Schranz, Inc.	Roofing - Manufacturing	\$559,280	\$132,460	23.7%
P.L. Freeman Co.	MM Schranz, Inc.	Roofing - Ofc., Parking, Bridge	\$258,661	\$258,661	100.0%
Price & Sons, Inc.	Cornerstone One, LLC	Material Supplier	\$199,430		0.0%
Ram's Contracting LTD	Hunzinger Construction Co.	Trash Removal and Misc. Trucking	\$121,053	\$68,951	57.0%
Rockwell Mechanical, LLC	Grunau Co.	HVAC Office & Parking Deck	\$1,616,458	\$1,342,000	83.0%
Rockwell Mechanical, LLC	Cornerstone One, LLC	Vapor Barrier - Office	\$22,207	\$22,207	100.0%
Rodriguez Coonstruction Co.	Payne & Dolan, Inc.	Asphalt Labor	\$5,000		0.0%
Security Officer Services, Inc.	Hunzinger Construction Co.	Site Security	\$160,000	\$65,508	40.9%
South Star Trucking, Inc.	Payne & Dolan, Inc.	Trucking - Asphalt	\$54,350		0.0%
SPE, Inc.	Avantti Design Group, LLC	Steel Erection - Building	\$5,353,761	\$4,345,361	81.2%
SPE, Inc.	Daigle Brothers, Inc.	Steel Erection - Office	\$1,195,415	\$1,195,415	100.0%
SPE, Inc.	Doral Corp.	Steel Erection - Bridge	\$412,400		0.0%
Straightline Grading & Excavating, LLC	Cornerstone One, LLC	Trucking	\$150,000		0.0%
Straightline Grading & Excavating, LLC	A.W. Oakes & Son	Mass Grading	\$1,609,690	\$695,640	43.2%
Szada Trucking, Inc.	Cornerstone One, LLC	Trucking / Hauling - Site Utilities	\$182,262	\$182,262	100.0%
Szada Trucking, Inc.	Cornerstone One, LLC	Trucking / Hauling - Office Plumbing	\$68,440	\$50,435	73.7%
Szada Trucking, Inc.	Cornerstone One, LLC	Trucking / Hauling - Manufacturing Plumbing	\$770	\$770	100.0%
Szada Trucking, Inc.	Cornerstone One, LLC	Trucking / Hauling - Office Excavation	\$543,125	\$543,125	100.0%
Szada Trucking, Inc.	Cornerstone One, LLC	Trucking / Hauling - Parking Excavation	\$40,050		0.0%
Szada Trucking, Inc.	Cornerstone One, LLC	Trucking / Hauling - Bridge Excavation	\$6,425		0.0%
Szada Trucking, Inc.	Cornerstone One, LLC	Trucking / Hauling - Bay 1-4 Excavation	\$139,740		0.0%
Szada Trucking, Inc.	Cornerstone One, LLC	Trucking / Hauling - Bay 5 Excavation	\$107,188		0.0%
Szada Trucking, Inc.	Cornerstone One, LLC	Trucking / Hauling - Monument Excavation	\$6,383		0.0%

TABLE 4 cont.: SBE CONSTRUCTION INCLUSION through June 2021

SBE Firm	Contracted by	Scope of Work	SBE Contract Value	SBE Paid to Date	% of Contract paid through June 2021
Thomas A. Mason Company, Inc.	Hunzinger Construction Co.	Painting	\$1,973,682	\$280,357	14.2%
Thomas A. Mason Company, Inc.	Hunzinger Construction Co.	Flooring	\$1,203,073	\$280,357	23.3%
Toki & Associates, Inc.	Hunzinger Construction Co.	Survey & Layout	\$40,000	\$25,150	62.9%
Toki & Associates, Inc.	Cornerstone One, LLC	Survey & Layout - Site Utilities	\$38,140	\$38,140	100.0%
Vazcaino's Trucking, LLC	Payne & Dolan, Inc.	Trucking - Asphalt	\$13,100		0.0%
ZS, LLC	Michels Corp.	Survey & Documentation	\$73,950	\$49,000	66.3%
ZS, LLC	Hunzinger Construction Co.	Roof Davits Manufacturing	\$236,500	\$25,439	10.8%
<b>SBE Construction Contracts Awarded to Date</b>			<b>\$63,410,314</b>	<b>\$39,420,441</b>	<b>62.2%</b>
<b>All Construction Contracts Awarded to Date</b>			<b>\$149,950,702</b>		
<b>SBE Construction Participation to Date</b>			<b>42.3%</b>	<b>Project Goal is 25%</b>	

\* S/DBE also has a certified sub contractor. Contract values shown are for self perform work only

## CONSTRUCTION SBE INCLUSION

GRAPH 3

### Contract Participation



25% SBE Goal

GRAPH 4

### Payments To Date



Electrician installing new wiring.

TABLE 5: TOTAL RPP PARTICIPATION through June 2021

Contractor	Contracted by	Scope of Work	Total Hours	RPP Hours	RPP %	Bonus Hours	RPP w/ Bonus Hours	RPP/SIA Hours	RPP/SIA %
30th State, LLC	MJM Truckin' LLC	Trucking	63.0	0.0	0.0%	0.0	0.0%	0.0	0.0%
ADG	Hunzinger Construction Co.	Fabrication & Installation	4,471.8	866.5	19.4%	209.7	24.1%	225.0	26.0%
Alex Simply Trucking, LLC	MJM Truckin' LLC	Trucking	188.5	188.5	100.0%	84.8	145.0%	188.5	100.0%
Area Erectors	Spancrete, Inc.	Steel & Precast Erector	2,637.0	1,078.0	40.9%	407.2	56.3%	390.0	36.2%
Arrow Crete Construction	Cornerstone Plumbing	Concrete Work	31.5	0.0	0.0%	2.9	9.3%	0.0	0.0%
A.W. Oakes & Sons, Inc.	Hunzinger Construction Co.	Mass Grading	12,302.0	5,185.5	42.2%	1,979.3	58.2%	1,733.0	33.4%
Chilstrom Erecting Corp.	Duwe Metal Products	Rebar	11,327.0	3,109.0	27.4%	988.2	36.2%	1,732.5	55.7%
Construction Services of Milwaukee, LLC	Michels Corp.	Structural Steel Furnish & Install	2,197.0	2,005.5	91.3%	892.9	131.9%	141.5	7.1%
Cornerstone Plumbing	Hunzinger Construction Co.	Footing Excavation	17,573.2	4,896.5	27.9%	1,514.2	36.5%	1,385.2	28.3%
C.M. Morris Group, Inc.	Hetzel-Sanfilippo, Inc.	Fireproofing & Spray Foam Insulation	877.0	62.0	7.1%	0.0	7.1%	0.0	0.0%
Dairyland Energy Solutions, Inc.	Cornerstone Plumbing	Fixture Installation	338.0	338.0	100.0%	152.1	145.0%	0.0	0.0%
David Bartel Trucking, Inc.	MJM Truckin' LLC	Trucking	19.3	0.0	0.0%	0.0	0.0%	0.0	0.0%
Delgado Trucking	MJM Truckin' LLC	Trucking	467.0	467.0	100.0%	210.2	145.0%	467.0	100.0%
Design Build Fire Protection	Hunzinger Construction Co.	Fire Protection	3,143.5	1,423.0	45.3%	554.3	62.9%	0.0	0.0%
Doral Corp.	Construction Services of Milwaukee, LLC/ Hunzinger Construction Co.	Welding Piles	1,117.0	1,117.0	100.0%	502.7	145.0%	1,081.0	96.8%
Duwe Metal Products	Hunzinger Construction Co./ Klein-Dickert Milwaukee, Inc./ Superior Masonry	Reinforcing Steel/ Window System/ Concrete Slabs	5,585.3	2,680.0	48.0%	1,060.7	67.0%	2,494.5	93.1%
Edra Trucking, LLC	MJM Truckin' LLC	Trucking	307.5	272.0	88.5%	120.6	127.7%	272.0	100.0%
Express Insulation	Cornerstone Plumbing	Insulation Installation	605.0	404.0	66.8%	171.8	95.2%	0.0	0.0%
Gordon Solutions, LLC	Klein-Dickert Milwaukee, Inc.	Glass Installation and Glazing	502.3	502.3	100.0%	226.0	145.0%	40.0	8.0%
Grunau Company	Hunzinger Construction Co.	Fire Protection & Mechanical Systems	10,192.3	5,096.0	50.0%	2,038.4	70.0%	477.5	9.4%
Guin's Trucking, LLC	MJM Truckin' LLC	Trucking	23.5	0.0	0.0%	0.0	0.0%	0.0	0.0%
Hard Rock Sawing	Cornerstone Plumbing	Site Utilities	53.0	0.0	0.0%	0.0	0.0%	0.0	0.0%
Helmrick's Trucking, LLC	MJM Truckin' LLC	Trucking	30.5	0.0	0.0%	0.0	0.0%	0.0	0.0%
Hetzel-Sanfilippo, Inc.	Hunzinger Construction Co.	Insulation Contractor	20,887.3	10,170.5	48.7%	4,040.9	68.0%	6,116.5	60.1%
HI & J Trucking, LLC	MJM Truckin' LLC	Trucking	71.5	0.0	0.0%	32.2	45.0%	0.0	0.0%
Hillside Damproofing	Hunzinger Construction Co.	Waterproofing Machine Bases	218.3	0.0	0.0%	0.0	0.0%	0.0	0.0%
Hunzinger Construction Co.	N/A	General Contractor	53,143.5	26,558.0	50.0%	10,629.3	70.0%	5,661.5	21.3%
HVA Products, Inc.	Grunau Company/ Lee Plumbing Mechanical	HVAC Installation	1,318.0	639.0	48.5%	253.6	67.7%	0.0	0.0%
Insulation Industries, Inc.	Grunau Company	Furnish/Install HVAC Controls	3,000.5	1,967.5	65.6%	833.7	93.4%	689.5	35.0%
Ivan's Trucking, LLC	MJM Truckin' LLC	Trucking	182.5	182.5	100.0%	82.1	145.0%	182.5	100.0%
JCP Construction	Hunzinger Construction Co./ Muza Sheet Metal Co.	Foundation Concrete/ Labor	5,801.5	3,769.5	65.0%	1,594.7	92.5%	1,726.0	45.8%
JLS Truckin' LLC	MJM Truckin' LLC	Trucking	282.3	282.3	100.0%	127.0	145.0%	282.3	100.0%
Jose G Mora Trucking, LLC	MJM Truckin' LLC	Trucking	16.0	0.0	0.0%	0.0	0.0%	0.0	0.0%
JRA Construction, LLC	Cornerstone Plumbing	Trucking	139.0	0.0	0.0%	0.0	0.0%	0.0	0.0%
Klein-Dickert Milwaukee, Inc.	Hunzinger Construction Co.	Glass & Glazing Services	7,190.8	2,729.5	38.0%	1,005.2	51.9%	868.0	31.8%


TABLE 5 Cont.: TOTAL RPP PARTICIPATION through June 2021

Contractor	Contracted by	Scope of Work	Total Hours	RPP Hours	RPP %	Bonus Hours	RPP w/ Bonus Hours	RPP/SIA Hours	RPP/SIA %
Lee Plumbing Mechanical Contractors, Inc.	Hunzinger Construction Co.	HVAC & Electrical Work	1,140.0	140.5	12.3%	13.3	13.5%	0.0	0.0%
M. M. Schranz Roofing, Inc.	Hunzinger Construction Co.	Commercial Roofing & Waterproofing	5,740.5	2,476.0	43.1%	951.0	59.7%	665.5	26.9%
Michels Corp.	Hunzinger Construction Co.	Pile Driving	32,867.0	12,511.5	38.1%	4,574.7	52.0%	4,196.5	33.5%
MJM Truckin' LLC	Straightline Grading & Excavating, LLC	Trucking	1,347.8	1,347.8	100.0%	606.5	145.0%	0.0	0.0%
Moras Trucking Uno, LLC	MJM Truckin' LLC	Trucking	436.3	382.3	87.6%	169.3	126.4%	382.3	100.0%
Muza Sheet Metal	Hunzinger Construction Co.	Sheet Metal Supplier	1,426.5	0.0	0.0%	0.0	0.0%	0.0	0.0%
P.L. Freeman Co.	Cornerstone Plumbing/ M.M. Schranz, Inc./ Lee Plumbing Mechanical	Site Utilities/ Roofing	573.5	521.5	90.9%	232.1	131.4%	173.5	33.3%
PCI Austad & Son, Inc.	Hunzinger Construction Co.	Acoustic Ceiling Installation	2,092.5	887.0	42.4%	338.9	58.6%	244.0	0.0%
R & C Trucking, LLC	MJM Truckin' LLC	Trucking	40.0	0.0	0.0%	0.0	0.0%	0.0	0.0%
RD Construction of WI, LLC	MJM Truckin' LLC	General Contractor	19.8	0.0	0.0%	0.0	0.0%	0.0	0.0%
Rock Solid Stabilization & Reclamation, Inc.	A.W. Oakes & Sons, Inc.	Reclamation Contractor	71.5	0.0	0.0%	0.0	0.0%	0.0	0.0%
Rockwell Mechanical	Grunau Company/ Cornerstone Plumbing	HVAC/ Plumbing Systems	1,191.3	518.0	43.5%	199.4	60.2%	0.0	0.0%
S. Sanchez Trucking	MJM Truckin' LLC	Trucking	47.0	0.0	0.0%	0.0	0.0%	0.0	0.0%
Sid's Sealants	Klein-Dickert Milwaukee, Inc.	Sealing Window Systems	224.5	0.0	0.0%	0.0	0.0%	0.0	0.0%
SOS Security Officer Services, Inc.	Hunzinger Construction Co.	Security Services	2,626.5	2,130.3	81.1%	933.8	116.7%	1,511.8	71.0%
SPE Inc. - Grunau	Daigle Brothers, Inc./ ADG/ Doral Corp./ Duwe Metals	Steel Erection	50,663.6	21,061.6	41.6%	7,997.6	57.4%	6,663.1	31.6%
Staff Electric	Hunzinger Construction Co.	Manufacturing & Bridge HVAC	5,136.0	4,779.5	93.1%	2,133.0	134.6%	894.0	0.0%
Straightline Grading & Excavating, LLC	A.W. Oakes & Sons, Inc./ Cornerstone Plumbing	Mass Grading/ Trucking	5,385.3	467.5	8.7%	0.0	8.7%	0.0	0.0%
Superior Masonry	Hunzinger Construction Co.	Masonry & Concrete Construction	3,310.5	1,522.5	46.0%	595.7	64.0%	828.0	54.4%
Surf Prep	Hunzinger Construction Co.	Painter	732.9	0.0	0.0%	0.0	0.0%	0.0	0.0%
Szada Trucking, Inc.	Cornerstone Plumbing	Trucking	7,907.5	7,876.8	99.6%	3,543.0	144.4%	6,546.3	83.1%
Terminal-Andrae, Inc.	Hurt Electric	Electrical Work	10,775.5	5,839.5	54.2%	2,381.0	76.3%	1,254.5	21.5%
Thomas A. Mason Co., Inc.	Hunzinger Construction Co.	Flooring Installation & Wall Coverings	3,096.0	1,456.5	47.0%	573.5	65.6%	1,246.0	85.5%
Waukesha Air & Vapor Barrier, Inc.	Hetzel-Sanfilippo, Inc.	General Contractor	532.0	237.0	44.5%	91.9	61.8%	237.0	100.0%
Yakov and Tina, Inc.	MJM Truckin' LLC	Trucking	8.3	0.0	0.0%	0.0	0.0%	0.0	0.0%
<b>Totals</b>			<b>312,473.8</b>	<b>145,011.7</b>	<b>46.4%</b>	<b>57,045.8</b>	<b>64.7%</b>	<b>53,575.9</b>	<b>36.9%</b>

## RPP INCLUSION

GRAPH 5


### RPP Inclusion

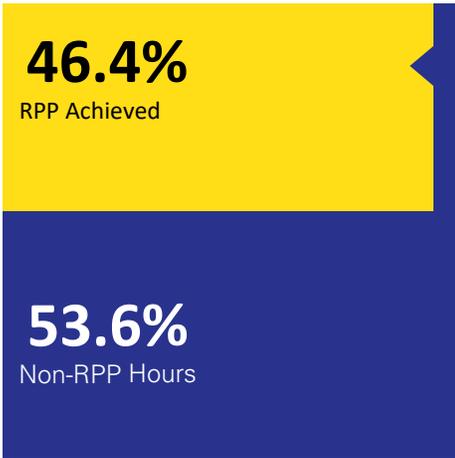

312,473.76 Total hours worked  
40% RPP Requirement


GRAPH 6

### RPP Inclusion w/ Bonus

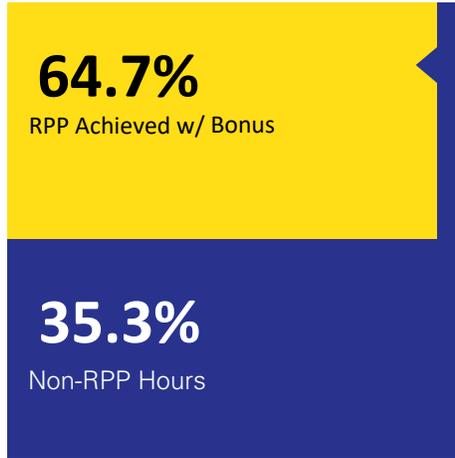

GRAPH 7

### RPP SIA Inclusion

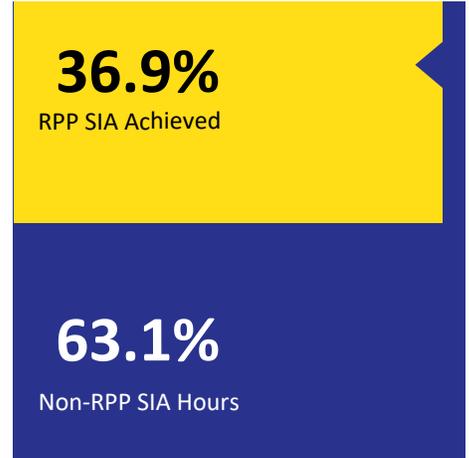

25% RPP SIA Requirement



Wall finisher completing her job.

TABLE 6: RPP PARTICIPATION BY ZIP CODE &amp; TRADE through June 2021

Zip Code & Trade	# of RPP Workers	Total RPP Hours
<b>Zip Code 53202</b>		
Heat or Frost Insulator	1	8.0
Ironworker	4	2,453.5
Plumber	1	338.0
<b>53202 Total</b>	<b>6</b>	<b>2,799.5</b>
<b>Zip Code 53204</b>		
Bricklayer	1	453.5
Carpenter	3	1,322.0
Heat or Frost Insulator	1	689.5
Ironworker	1	649.5
Laborer	1	1,101.5
Piledriver	1	746.5
Truck Driver	3	1,925.8
Tuckpointer	1	72.0
<b>53204 Total</b>	<b>12</b>	<b>6,960.2</b>
<b>Zip Code 53205</b>		
Carpenter	1	1,969.0
Laborer	2	1,307.5
<b>53205 Total</b>	<b>3</b>	<b>3,276.5</b>
<b>Zip Code 53206</b>		
Carpenter	2	931.5
Cement Finisher	1	82.0
Ironworker	2	2,264.0
Laborer	2	800.8
Sheet Metal Worker	1	205.5
Truck Driver	1	179.0
<b>53206 Total</b>	<b>9</b>	<b>4,462.8</b>
<b>Zip Code 53207</b>		
Carpenter	5	4,741.5
Cement Finisher	1	53.5
Electrician	4	1,971.0
Heavy Equipment Operator	2	1,840.0
Ironworker	2	1,033.5
Laborer	2	2,144.8
Piledriver	2	2,793.0
Plumber	1	570.3
Roofer	1	162.5
Steamfitter	1	930.0
Teledata Technician or Installer	1	632.0
Truck Driver	2	376.0
<b>53207 Total</b>	<b>24</b>	<b>17,248.0</b>

Zip Code & Trade	# of RPP Workers	Total RPP Hours
<b>Zip Code 53208</b>		
Acoustic Ceiling Tile Installer	1	32.0
Carpenter	1	1,300.0
Electrician	1	769.5
Ironworker	4	1,456.0
Laborer	3	570.0
Millwright	1	800.0
Sheet Metal Worker	1	240.0
<b>53208 Total</b>	<b>12</b>	<b>5,167.5</b>
<b>Zip Code 53209</b>		
Acoustic Ceiling Tile Installer	1	291.0
Electrician	1	272.0
Heavy Equipment Operator	2	1,190.5
Ironworker	1	151.0
Laborer	2	689.0
<b>53209 Total</b>	<b>7</b>	<b>2,593.5</b>
<b>Zip Code 53210</b>		
Bricklayer	1	696.0
Electrician	1	582.5
Heavy Equipment Operator	1	280.5
Ironworker	1	456.5
Plumber	1	8.0
<b>53210 Total</b>	<b>5</b>	<b>2,023.5</b>
<b>Zip Code 53211</b>		
Acoustic Ceiling Tile Installer	1	447.0
Electrician	1	309.5
Ironworker	2	1,088.0
Plumber	1	37.5
Project Engineer (Non-construction)	2	2,334.0
<b>53211 Total</b>	<b>7</b>	<b>4,216.0</b>
<b>Zip Code 53212</b>		
Acoustic Ceiling Tile Installer	1	244.0
Carpenter	5	1,379.5
Electrician	2	1,578.5
Glazier	1	868.0
Ironworker	6	2,850.5
Laborer	2	294.0
Truck Driver	2	179.8
<b>53212 Total</b>	<b>19</b>	<b>7,394.3</b>

TABLE 6 Cont.: RPP PARTICIPATION BY ZIP CODE &amp; TRADE through June 2021

Zip Code & Trade	# of RPP Workers	Total RPP Hours
<b>Zip Code 53213</b>		
Electrician	1	1,443.0
Ironworker	1	60.5
Steamfitter	3	2,328.5
<b>53213 Total</b>	<b>5</b>	<b>3,832.0</b>
<b>Zip Code 53214</b>		
Electrician	1	884.0
Fire Sprinkler Fitter	1	993.0
Heat or Frost Insulator	2	1,278.0
Ironworker	2	1,052.5
Laborer	1	1,561.5
Painter	1	130.5
<b>53214 Total</b>	<b>8</b>	<b>5,899.5</b>
<b>Zip Code 53215</b>		
Bricklayer	1	196.0
Carpenter	6	2,970.5
Drywall Taper or Finisher	1	584.0
Heavy Equipment Operator	2	3,004.5
<b>Ironworker</b>	<b>6</b>	<b>4,109.6</b>
Laborer	5	1,460.8
Painter	4	1,858.8
Roofer	1	665.5
Truck Driver	15	6,036.3
Tuckpointer	2	492.5
<b>53215 Total</b>	<b>43</b>	<b>21,378.4</b>
<b>Zip Code 53216</b>		
Carpenter	5	5,578.5
Electrician	1	463.0
Laborer	5	1,416.5
Millwright	1	36.0
Truck Driver	1	1,347.8
<b>Total 53216</b>	<b>13</b>	<b>8,841.8</b>

Zip Code & Trade	# of RPP Workers	Total RPP Hours
<b>Zip Code 53218</b>		
Bricklayer	1	9.5
Carpenter	2	1,448.3
Electrician	1	585.0
Heavy Equipment Operator	2	701.0
Ironworker	2	1,101.0
Laborer	1	270.5
Piledriver	1	1,064.0
Plasterer	1	12.0
Plumber	1	933.9
Roofer	1	659.0
Truck Driver	1	246.3
<b>53218 Total</b>	<b>14</b>	<b>7,030.5</b>
<b>Zip Code 53219</b>		
Carpenter	1	378.5
Cement Finisher	1	366.0
Drywall Taper or Finisher	2	1,050.0
Electrician	1	272.0
Fire Sprinkler Fitter	1	184.0
Glazier	1	379.8
Heavy Equipment Operator	3	2,955.5
Ironworker	3	1,551.5
Laborer	3	2,002.8
Roofer	1	642.5
Sheet Metal Worker	1	140.5
<b>53219 Total</b>	<b>18</b>	<b>9,923.0</b>
<b>Zip Code 53220</b>		
Electrician	2	599.5
Glazier	1	978.8
Ironworker	2	937.5
Roofer	1	346.5
<b>53220 Total</b>	<b>6</b>	<b>2,862.3</b>
<b>Zip Code 53221</b>		
Acoustic Ceiling Tile Installer	1	352.0
Carpenter	2	1,880.5
Electrician	3	1,385.0
Heavy Equipment Operator	2	1,506.0
Ironworker	1	28.0
Laborer	2	845.5
Sheet Metal Worker	1	1,051.0
Truck Driver	2	512.5
<b>53221 Total</b>	<b>14</b>	<b>7,560.5</b>

TABLE 6 Cont.: RPP PARTICIPATION BY ZIP CODE & TRADE through June 2021

Zip Code & Trade	# of RPP Workers	Total RPP Hours
<b>Zip Code 53222</b>		
Carpenter	1	900.5
Cement Finisher	1	270.0
Electrician	2	957.0
Fire Sprinkler Fitter	1	246.0
Ironworker	2	480.5
Piledriver	1	449.0
Plumber	2	1,181.6
Sheet Metal Worker	1	380.0
<b>53222 Total</b>	<b>11</b>	<b>4,864.6</b>

<b>Zip Code 53223</b>		
Glazier	1	503.0
Ironworker	2	1,443.5
Laborer	1	1,380.5
<b>53223 Total</b>	<b>4</b>	<b>3,327.0</b>

<b>Zip Code 53224</b>		
Carpenter	1	2,138.5
Carpet Layer	1	80.0
Electrician	1	599.0
Ironworker	1	1,440.0
Truck Driver	1	195.8
<b>53224 Total</b>	<b>5</b>	<b>4,453.3</b>

<b>Zip Code 53225</b>		
Electrician	1	639.0
Laborer	2	321.0
<b>53225 Total</b>	<b>3</b>	<b>960.0</b>

<b>Zip Code 53227</b>		
Carpenter	2	1,116.5
Laborer	2	1,995.5
<b>53227 Total</b>	<b>4</b>	<b>3,112.0</b>

<b>Zip Code 53228</b>		
Cement Finisher	1	976.0
Heat or Frost Insulator	1	396.0
Ironworker	2	490.5
Plasterer	1	50.0
<b>53228 Total</b>	<b>5</b>	<b>1,912.5</b>

Zip Code & Trade	# of RPP Workers	Total RPP Hours
<b>Zip Code 53233</b>		
Carpenter	1	1,014.8
Project Engineer (Non-construction)	1	1,898.5
<b>53233 Total</b>	<b>2</b>	<b>2,913.3</b>
<b>TOTALS*</b>	<b>259</b>	<b>145,011.7</b>

\* Actual number of unique workers is 254, as two workers resided in multiple zip codes and three workers have multiple trades.



Carpenters working in tandem.
