# **CDA Scattered Sites MKE**

SBE, RPP and Section 3
Participation Performance Report
through December 31, 2024



**Submitted by:** 




**Date:** January 19, 2025

### **Project Summary**


The Milwaukee Habitat CDA Scattered Sites Project consists of 40 scattered site affordable housing units built in 20 new construction duplexes in Midtown neighborhood of Milwaukee, Wisconsin.

Developer:	Emem Group, LLC
Project Address:	Various lots in the Midtown Neighborhood
Professional Services Cost Subject to Inclusion	\$362,355
Applicable Professional Services Payments to Date	\$256,794
Construction Cost Subject to Inclusion	\$6,386,061
Applicable Construction Draw to Date	\$1,245,851

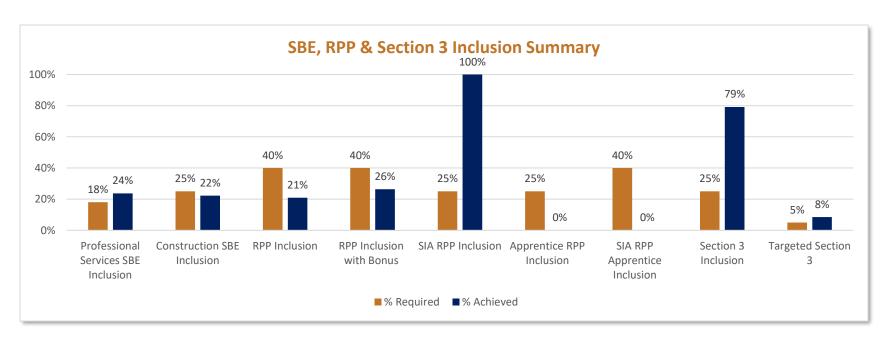

#### **SBE Professional Services Inclusion**

Through the period covered by this report, this project has achieved 24% SBE participation for Professional Services, which exceeds the 18% inclusion requirement.




Total Value of SBE Payments	Goal/Requirement	Actual	Status
SBE Participation Percentage	18%	24%	+6%
Value of SBE Participation	\$65,224	\$85,875	+\$20,651

**Table 1: Professional Services SBE Inclusion** 

			SERVICE PERFORMED OR	SUBCONTRACT		NTRACT TOTAL AMOU	
NAME OF CERTIFIED FIRM	DBE/SBE	SUBCONTRACTOR OF	MATERIALS SUPPLIED	AWARD AMOUNT		PAID T	O DATE
Cross Management Services, Inc.	DBE/SBE	Emem Group LLC	Inclusion Consultant	\$	85,875	\$	9,168
TOTAL INCLUSION			\$	85,875	\$	9,168	
INCLUSION, AS PERCENT OF PROFESSIONAL SERVICES COST SUBJECT TO INCLUSION					24%		
INCLUSION, AS PERCENT OF PROFESSIONAL SERVICES DRAW TO DATE					4%		

#### **SBE Construction Inclusion**

Through the period covered by this report, this project has awarded 22% of the contracts to SBE firms. As additional contracts are awarded, the 25% SBE inclusion will be achieved.



Total Value of SBE Payments	Goal/Requirement	Actual	Status
SBE Participation Percentage	25%	22%	-3%
Value of SBE Participation	\$1,596,515	\$1,421,300	-175,215

**Table 2: Construction SBE Inclusion** 

NAME OF OFFICIED FIRM	DDE (ODE	OUDOONTDAOTOD OF	SERVICE PERFORMED OR		SUBCONTRACT		OTAL AMOUNT
NAME OF CERTIFIED FIRM	DBE / SBE	SUBCONTRACTOR OF	MATERIALS SUPPLIED	A	WARD AMOUNT	PP	AID TO DATE
A & A Plumbing of Milwaukee LLC	DBE/SBE	MESH Construction LLC	Plumbing (Rough & Finish)	\$	570,000	\$	15,918
Devix Heating and Cooling LLC	SBE	MESH Construction LLC	HVAC (Rough & Finish)	\$	469,380	\$	-
Dekoven Enterprises, LLC	DBE/SBE	MESH Construction LLC	Roofing	\$	114,785	\$	1
Jordans Construction Services LLC	DBE/SBE	MESH Construction LLC	Interior Finish Carpentry Labor	\$	156,000	\$	-
Rodriguez Landscape Company	DBE/SBE	MESH Construction LLC	Site Clearing	\$	22,903	\$	15,786
Rodriguez Landscape Company	DBE/SBE	MESH Construction LLC	Grading	\$	19,288	\$	-
Rodriguez Landscape Company	DBE/SBE	MESH Construction LLC	Planting (Landscaping)	\$	68,944	\$	-
TOTAL INCLUSION				\$	1,421,300	\$	31,704
INCLUSION, AS PERCENT OF CONSTRUCTION COST SUBJECT TO INCLUSION 22%							
INCLUSION, AS PERCENT OF CONST	TRUCTION D	RAW TO DATE					3%

## **RPP Participation**

As shown in Table 3 below, the RPP inclusion achieved is 21% and 26% when the bonus hours for SIA RPP hours are included.

**Table 3: RPP Participation by Contractor** 

	Trade	On-Site Construction Hours						
Contractor		Total Hours	RPP Worker	RPP %	SIA RPP	SIA RPP %		
		Worked	Hours		Hours			
A&A Plumbing of Milwaukee, LLC	Plumbing	40.00	-		-			
Devix Heating & Cooling LLC	HVAC	125.00	-		-			
Eduardos Tree Service LLC	Site Clearing	168.00	-		-			
Emem Group LLC	Construction Labor	687.00	607.00	88%	607.00	100%		
Friemoth Concrete Corp.	Excavation & Fill, Concrete Foundation	1,887.42	-		-			
Total Hours		2,907.42	607.00	21%	607.00	100%		
Bonus SIA RPP Hours			158.13					
Bonus Apprentice RPP Hours			-					
Total RPP Hours with Bonus		2,907.42	765.13	26%				

**Table 4: RPP Participation by Craft** 

Craft	RPP Hours	# of RPP Workers
Carpenter	360.00	1
Laborer	247.00	1
Total	607.00	2

**Table 6: RPP Participation by Race** 

Race	RPP Hours	# of RPP Workers
African American	607.00	2
Total	607.00	2

**Table 5: RPP Participation by Zip Code** 

Zip Code		# of RPP Workers
53210	607.00	2
Total	607.00	2

**Table 7: RPP Participation by Gender** 

Gender	RPP Hours	# of RPP Workers
Male	607.00	2
Total	607.00	2

## **Section 3 Participation**

As shown in Table 8 below, the Section 3 inclusion achieved is 79% and Targeted Section 3 inclusion is 8%.

**Table 8: Section 3 Worker Inclusion** 

	Trade	On-Site Construction Hours					
Contractor		Total Hours	Section 3	% Section 3	Targeted	%	
		Worked	Worker Hours	% Section 3	Section 3	Targeted	
A&A Plumbing of Milwaukee, LLC	Plumbing	40.00	-				
Devix Heating & Cooling LLC	HVAC	125.00	-				
Eduardos Tree Service, LLC	Site Clearing	168.00	168.00	100%			
Emem Group, LLC	Construction Labor	687.00	247.00	36%	247.00	36%	
Friemoth Concrete Corp.	Excavation & Fill, Concrete Foundation	1,887.42	1,887.42	100%			
Total Hours		2,907.42	2,302.42	79%	247.00	8%	
