

# The Corliss



## Participation Report Through September 2024

The Corliss project is a 576-unit Affordable Housing New Construction project at the Filer & Stowell complex southeast of South First and East Becher streets in the Bay View /Harbor District neighborhood of Milwaukee.

The project is led by Bear Development (Bear), with Construction Management Associates (CMA) as the construction manager. Prism Technical Management & Marketing Services, LLC (Prism) has been contracted to assist in the achievement of project inclusion requirements: 40% RPP workforce; and contract spend of 25% Construction and 18% Professional Services.

Bear is committed to the letter and spirit of the City of Milwaukee Human Resource Agreement requiring the utilization of Contractors, Consultants, and other service providers reflective of the diversity of the City of Milwaukee. This report is specific to the inclusion of firms certified by the City as SBE (or alternatively DBE) and deployment of local skilled trade persons in the workforce, certified by the City's Residents Preference Program.

While not the subject of this report it is noted that this development is also committed to meeting the goals under a Low-Income housing Tax Credit LIHTC agreement with WHEDA.



# SBE Professional Services Participation


Table 1: SBE Professional Services

Firm	Value Subject to Participation
Various	\$481,614

Project Subject to Participation:	\$481,614	
Required SBE Participation:	\$86,691	18.0%
Actual SBE Participation*:	\$326,272	67.6%

Consultant	Sub To	Scope	DBE	SBE	Awarded Contract Value
Prism Technical Management & Marketing Services, LLC	Bear Development	Inclusion Consultant	X	X	\$146,272
Construction ASAP, LLC	Construction Management Associates	Workforce Sourcing	X		\$180,000
TOTAL					\$326,272

Chart 1: SBE Participation

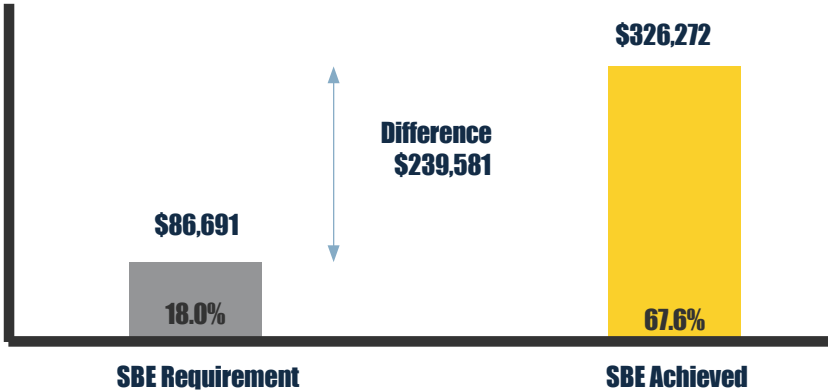

# SBE Construction Contract Participation

Table 2: Construction Contract


Firm	Contracted by	Scope of service	Value Subject to Participation
Construction Management Associates, Inc.	Bear Development	General Contractor	\$75,128,941
TOTAL			\$75,128,941

Table 3: SBE Construction Contracts

Contractor	Sub To	Scope	Awarded Contract Value
BRT Trucking	Cornerstone One, LLC	Hauling	\$317,928
Hernandez Roofing	Construction Management Associates, Inc.	Roofing	\$1,803,516
Insulation Technologies, Inc	Construction Management Associates, Inc.	Siding	\$2,506,956
P.L. Freeman	Quality Heating & Sheet Metal, Inc.	HVAC	\$4,632,900
Price And Sons, Inc.	Cornerstone One, LLC	Materials	\$442,761
Selarom Construction	Construction Management Associates, Inc.	Framing	\$13,113,988
On-Site Staffing	Construction Management Associates, Inc	Labor	\$70,654
On- Site Staffing	Kurk Concrete	Labor	\$1,686
TOTAL			\$22,890,388

Project Subject to Participation:	\$75,128,941	
Required SBE Participation:	\$18,782,235	25.0%
Actual SBE Participation:	\$22,890,388	30.5%




Chart 2: SBE Participation

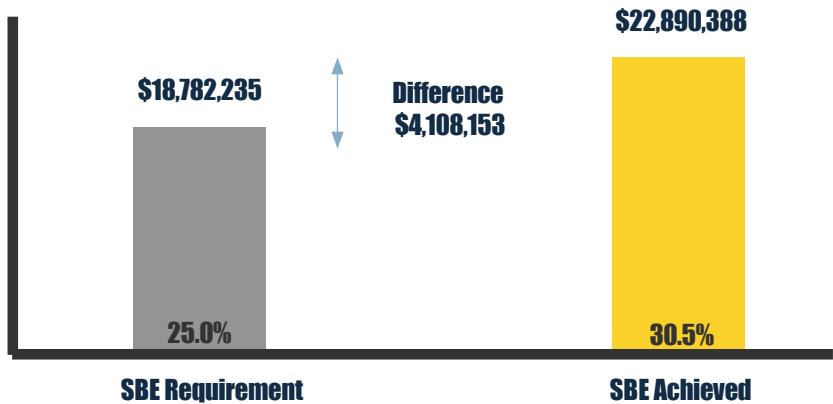

# Workforce Participation

Total Eligible Hours Worked:	21,160.7
RPP Participation:	44.4%
RPP SIA Participation:	38.4%
RPP with Bonus:	50.4%

Chart 3: Workforce Participation

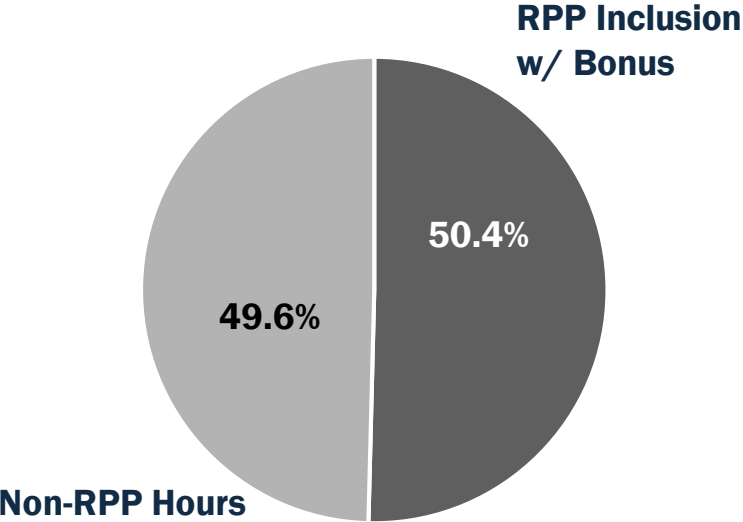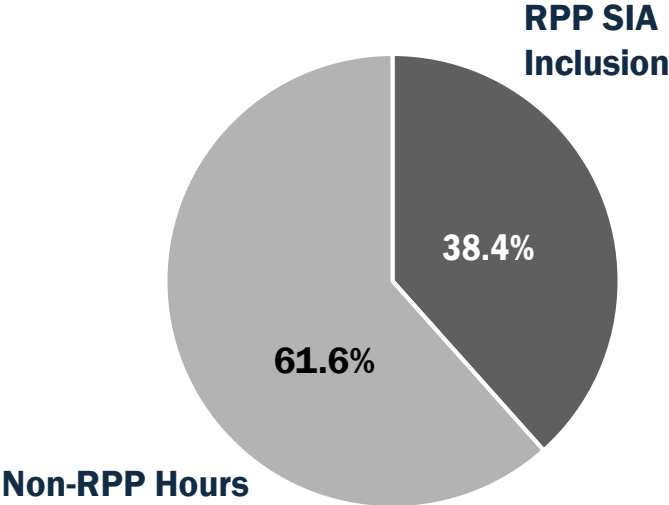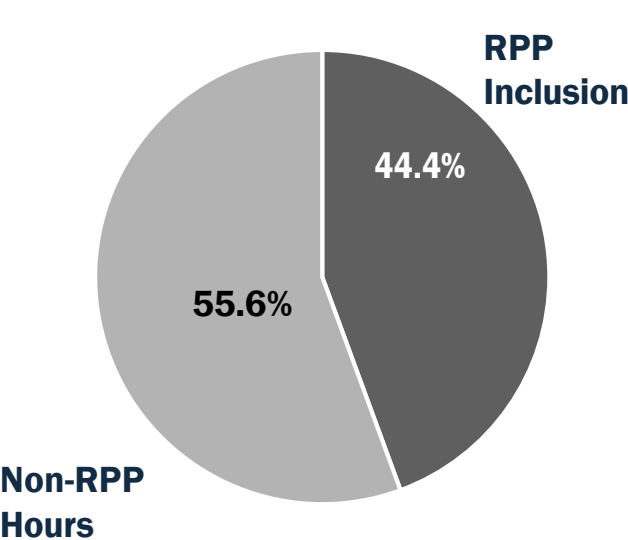



Thank you
