



Information Session:

Foxconn's Industrial Construction Work in Phase 1 of Area 1 of Wisconn Valley Science & Technology Park

April 2018





Agenda

- Foxconn
- Wisconsin Economic Development Corporation (WEDC)
- Gilbane Building Company and M+W Group
- Project Overview
- Schedule
- Wisconsin First
- Procurement Process
- Next Steps
- Questions and Answers



FOXCONN







Cares Moment



FOXCOM

FOXCONN IN WISCONSIN



ABOUT THE PROJECT



- Largest economic development project in Wisconsin history
- 13,000 jobs when campus is complete (avg. salary: \$53,000, plus benefits)
- 10,000 direct construction jobs annually over 4-6 years
- Science and Technology Park in Mt. Pleasant
- \$1.4 B annually in purchases from Wisconsin suppliers



PUBLIC INFRASTRUCTURE BID PROCESS

- Bid alerts communicated through Wisconn Valley News
- Register at wisconnvalley.wi.gov to be notified of bid opportunities






WATER MAIN, SEWER MAIN & DEMOLITION BID PROCESS

- Water Main = City of Racine Water Utility
 - Prequalification is required by the City of Racine Water Utility;
 call 262-636-9432 to request prequal forms
- Sewer Main & Demolition = Village of Mount Pleasant
 - Registration at http://www.mtpleasantwi.gov/DocumentCenter/View/622
- Pre-bid meetings/matchmaking
- Bids to be submitted with a Utilization Plan for review
- Bids "awarded to the lowest competent and responsible bidder"
 - Wis. Stat. s. 84.06(2)(a)



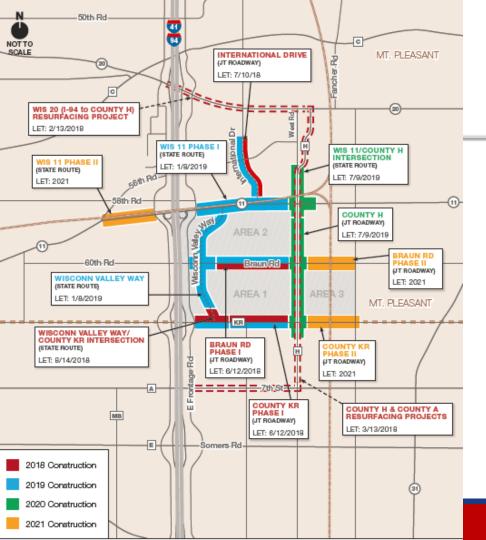

WisDOT LET Packages

14 packages

2018 construction includes:

- WIS 20 (I-94 to County H)- underway
- International Drive
- Braun Road (EB from east frontage road to WIS 11)
- County KR (EB east frontage road to County H)
- Wisconn Valley Way / County KR intersection
- County H and A resurfacing is underway



WisDOT OPPORTUNITIES - 2018

- Bidding for WisDOT highway construction projects is conducted under the authority provided in Wisconsin Statutes 84.06(2)(a) Bids, Contracts.
- Contracts awarded to the lowest competent and responsible contractors.
- WisDOT's bidding process on highway projects
- State of Wisconsin, Department of Transportation, Standard Specifications for Highway and Structure Construction
 - http://wisconsindot.gov/rdwy/stndspec/ss-01-02.pdf#ss102
 - Contractors checklist can be found at <u>http://wisconsindot.gov/hccidocs/bidder-approval-contractors-checklist.pdf</u>
- Highway construction bid lettings occur second Tuesday each month




WisDOT BIDDING PROCESS

- Bidders are prequalified by WisDOT
 http://wisconsindot.gov/hccidocs/prequalification-policy-June2011.pdf
- Bid letting advertisements posted about 5 weeks prior to the letting
- Plan holder and eligible bidder listings are posted 10 days prior to the letting date
- Bidders submit a sealed bid through Bid Express https://www.bidx.com/
- Highway construction projects have a bid opening. Upon opening and reading the prospective bids, the department posts apparent bids at approximately 9:30 a.m. on the day of the letting.





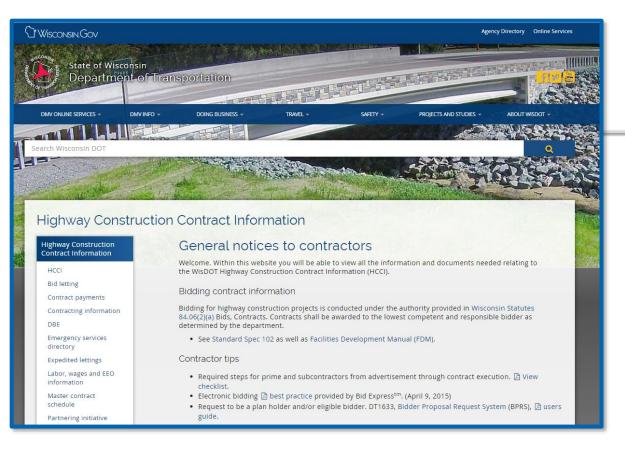

Visit WisDOT

- Roadway information please visit: www.projects.511wi.gov/
- Bid letting information please visit:
 www.wisconsindot.gov



PUBLIC INFRASTRUCTURE CONSTRUCTION & OPPORTUNITY FOR ALL

- Diverse talents and skills of Wisconsin's business and workforce, including emerging businesses and under-represented workers, are essential to maximize Wisconn Valley economic development potential
- All primes must submit a utilization plan prior to bid opening
 - Not a basis of bid evaluation; Must follow state & federal rules to retain funds & legality
- Advisory committee established to review plans, make recommendations, engage community and resources, and evaluate benefit
- Periodic public meetings will discuss progress and outcomes




SCALING UP SKILLED WORKFORCE

- Wisconsin Department of Workforce Development (DWD)
 Job Center of Wisconsin
 https://jobcenterofwisconsin.com/Presentation/Employers/Default.aspx
- Apprenticeship Training support https://dwd.wisconsin.gov/apprenticeship/contacts.htm
- Training grants for up to 50% of eligible costs through its Fast Forward program: http://wisconsinfastforward.com/wff standard.htm



SUPPLY CHAIN MARKETPLACE


- Online supply chain directory that enables companies to connect with suppliers and buyers
- Free, easy-to-use tool to create profiles, post RFPs, signup for newsletter and alerts
- Search by key industry directories and service categories



WISCONN VALLEY INFORMATION

Wisconnvalley.wi.gov

 Primary site for contractors to engage with public infrastructure and building construction



Wisconnvalley.wi.gov/newsletter

 Bi-weekly and breaking news updates on project developments



WISCONN VALLEY NEWS

The Wisconn Valley News is published every other week and designed to keep interested individuals up to date on Foxconn construction plans, infrastructure improvements, traffic pattern updates, and more. Local elected officials, suppliers, contractors and members of the public are encouraged to turn to the Wisconn Valley News for the latest project status, road updates, next steps, and interesting facts. When appropriate, special bulletins will also be distributed to ensure the most timely information possible.



Project Status



In November, Governor Scott Walker and Foxconn Chairman Teny Gou signed an agreement to bring a \$10 billion world-class advanced manufacturing campus and 13,000 jobs to Wisconsin. This project, called Wisconn Valley, is a once-in-a-lifetime opportunity, expected to have a transformational effect on our entire state.

Following the signed contract, Foxconn Technology Group deposited 580 million to purchase land in Mount Pleasant between WIS 11 and County KR. The project is underway and work is moving forward to create a campus that will build 7 million LCD units a year in Wisconsin. Foxconn is finalizing the design and construction plans for the campus, while state and local

governments are working to finalize plans for water, sewer, and roadways.





Information Session:

Foxconn's Industrial Construction Work in Phase 1 of Area 1 of Wisconn Valley Science & Technology Park

April 2018







Gilbane Building Company and M+W Group





1912 established



Leading global clean room builder



\$3.1 billion annual revenue



Present in 30+ countries

















Committed to building a

World Class Science & Technology Park

and put

Wisconsin First!

Information is proprietary and confidential to M+W | Gilbane A Joint Venture. Disclosure to other parties is prohibited without explicit consent











Working in Wisconsin since

1978 with an office located

in downtown Milwaukee

Largest Milwaukee-Area **Construction Firm** Business Journal of Milwaukee (2017)



280 **REGIONAL STAFF**

2,800 **GLOBAL STAFF**



Project Structure



SIO International Wisconsin, Inc.

The Wisconsin Economic Development Corporation Agreement

Development Agreement Village of Mount Pleasant, Racine County, Wisconsin








Ⅲ M+W GROUP

100's of Trade Contractors and Vendors

Gilbane







Contractual RelationshipInformation flow






Foxconn's Industrial Construction Work on Phase 1 in Area 1 of Wisconn Valley Science & Technology Park

- Foxconn construction work will begin on Phase 1 in Area 1 of the Advanced Display Manufacturing facilities in 2018
- Phase 1 consists of approximately 1,000 acres of site work and the construction of multiple buildings
- Phase 1 construction work, which will begin in spring 2018, is anticipated to be site work,
 material procurement, and temporary logistics preparation
- Vertical building construction work is anticipated to start in late 2018 or early 2019
- Procurement (bidding) for subcontractors, vendors, suppliers and professional services firms
 will follow a clear and detailed process with good faith efforts to place Wisconsin
 First while building significant capacity in both workforce and businesses





Site Areas Phase 1 of Area 1

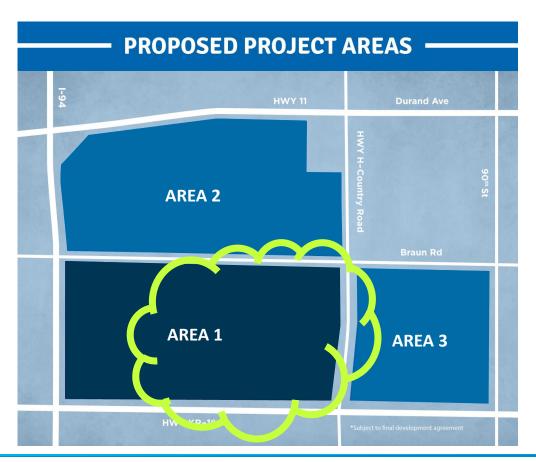






Phase 1, Area 1 Master Plan

Advanced Technology Display Facilities

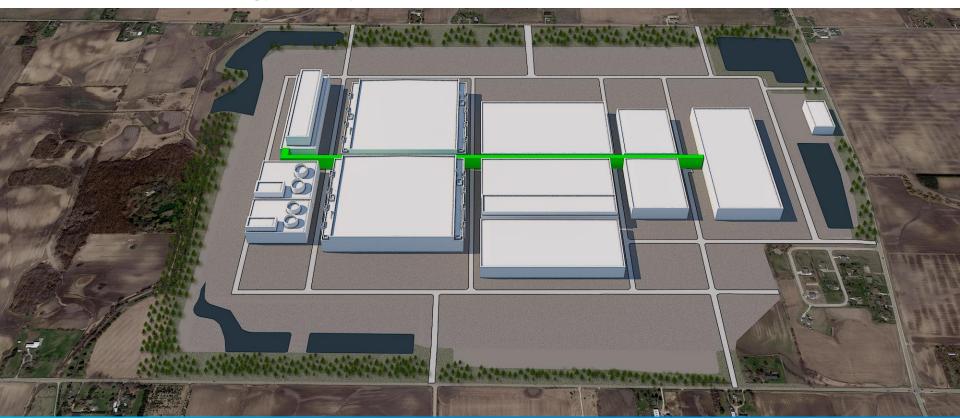





Site Development of Masterplan

Phase 1 of Area 1 – Mass Grading and Stormwater Management







Schedule

Process Programming

October 2017-June 2018

Full Release of Professional Team

- April 2018

Phase 1, Master Plan, Sitework, Infrastructure, Logistics

April/May 2018 Start

Phase 1, Advanced Display Manufacturing Facilities **Foundations**

Late 2018/Early 2019



Information is proprietary and confidential to M+W | Gilbane A Joint Venture. Disclosure to other parties is prohibited without explicit consent





Wisconsin First and Racine County Economic Inclusion and Diversity Goals



Business Contracting and Inclusion Goals

Wisconsin based Businesses	60%		
Racine County based Businesses	10%		
Minority-Owned (MBE) Business Enterprises			
oman-Owned (WBE) Enterprises 10% Combir			
Veteran-Owned Business Enterprises			

Workforce Inclusion and Diversity Goals

Information is proprietary and confidential to M+W | Gilbane A Joint Venture. Disclosure to other parties is prohibited without explicit consent

Wisconsin Resident Work Hours with an emphasis on Racine County Residents	70%		
Minorities or People of Color*			
Women	10% Combined		
Veterans]		

Gilbane Building Company and M+W Group will deploy best efforts through robust outreach, procurement and construction practices to achieve the goals for the construction projects awarded for their work in the Science and Technology Park.





Procurement Process

Contractor/Vendor Procurement








Robust, Detailed, Bidding Documents

- Proposal Form (issued via ibidpro)
- 2. Invitation to Bid
- 3. Confidentiality Agreement
- 4. General Instructions to Bidders
- 5. Project Schedule
- Advanced Planning & Scheduling Procedures
- 7. Site Logistics and Phasing Plans
- 8. Rules and General Scope of Work
- 9. Economic Inclusion Plan and Forms
- 10. Sample Trade Contract Agreement
- Supplemental Conditions to Trade Contract Agreement
- Sample Performance and Payment Bond Forms

- 13. Insurance Requirements
- 14. Billing Procedures with Textura Information
- 15. Cost Segregation
- 16. Project Safety Plan
- 17. BIM Guide (Standards)
- 18. Software Utilization
- 19. Project Quality Plan
- 20. Waste Management Plan
- 21. Geotechnical Report
- 22. Survey and Right of Way Control Exhibits
- 23. Drawing and Specification Log
- 24. Cash Flow Template
- 25. Manpower Projection Template

Information is proprietary and confidential to M+W | Gilbane A Joint Venture. Disclosure to other parties is prohibited without explicit consent

26. For Information Documents

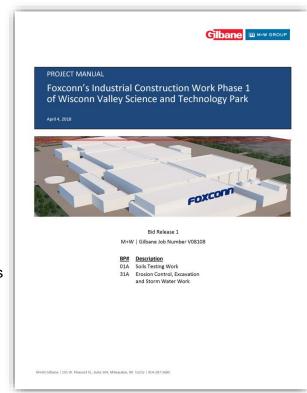





Scope Review Example

Detailed Bid Comparison and Scope Review


- Wisconsin First Economic Inclusion
- Pricing Breakdown
- General Items
- Specific Scope and Quantification
- Resources and Schedule
- Unit Prices
- Workforce and Cash Flow
- Terms & Conditions

	Flying Eagle 8.1.8 Array Building		
		Trade: 03A Con	crete
	M+W Gilbane	Name: XXXXX Telephone: 920-	924-2900
	Requested Scope	Email Address	XXXXXX@XXXXX.com
State Control ■ Intervention of Control of Control ■ Control ■ Control		Company: XXXXX Construction	
	REVISED SCOPE REVIEW 12/1/2017	Company. 7000	TOT CONSTRUCTION
	<u>BASE BID</u>		
rade: 0	3A Concrete		
		Included	Enter Yes or No
General:		or Excluded	and Exclusion
1	Specified products and manufacturers (no substitutions)	Inc.	Yes
2	Tax INCLUDED	Inc.	Yes
3	Onsite gen. liability and w/c insurance included	Inc.	Yes
4	Addenda No's1_,, included	Inc.	
5	RFI's1,2,, included	Inc.	Yes
6	Performance and Payment Bond EXCLUDED	EXCL.	Yes
7	Experience Modification Rate (EMR) <1.0 (provide EMR score) Each Trade Contractor shall include all clean-up of their own materials, waste and debris on	EMR	0.53
8	a daily basis. This Trade Contractor is responsible for his own clean-up. Clean-up includes sweeping, where required, to completely remove created debris. Pick-up debris immediately, breakdown cartons and dispose of properly. Clean-up is a contractual requirement and no written notification will be provided in the event of non-compliance.	Inc.	Yes
9	It is planned that this project will be seeking LEED Certification from the U.S. Green Building Council. To facilitate that submission, this Trade Contractor shall cooperate and provide all necessary documentation (i.e. cost breakdowns, material recycled content certification, and material origin certification) relevant to the work of this bid package	Inc.	Yes
10	Coordination with other trades including 15 minute preshift meeting, weekly foreman coordination meetings, and weekly project manager meetings	Inc.	Yes
11	Submittals, RFI's and Daily Reports shall be provided via Gilbane's I-build Management Software	Inc.	Yes





Recommendation of Award Example

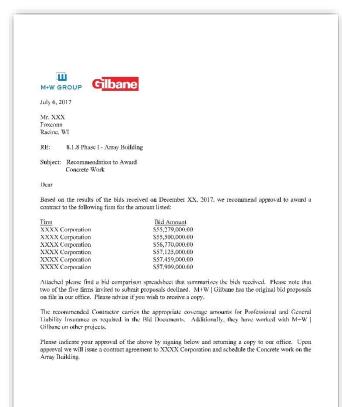

XX/XX/XXXX		
If you have any questions or require additional i	nformation, please do not hesitate to call	
Sincerely,		
M+W GILBANE A Joint Venture	Approved by:(Foxconn)	
Allen Ware Adam Jelen Project Principals	Date:	
ce: Project Purchasing Files Project Management and Field Staff		


Information is proprietary and confidential to M+W|Gilbane A Joint Venture. Disclosure to other parties is prohibited without explicit consent





Key Terms and Conditions

- Wisconsin First goals
- 30 day payment terms, with monthly draws
 - Bi-monthly draws will be processed where need is demonstrated and requested at the time of bid
- Foxconn's purchases of real property improvements, building materials, supplies, equipment, and landscaping services are exempted from Wisconsin sales and use tax
- Industry standard agreement terms and conditions

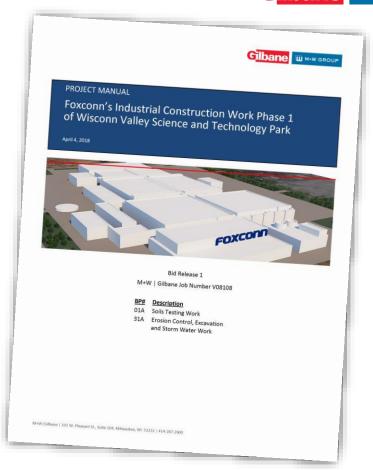



Next Steps

Bid Releases

Release 1: Ground Moving and Site Development Q2 2018

Release 2: Logistics and Temporary Facilities Q2-Q3 2018

Release 3: Site Utilities and Roadways Q3-Q4 2018

Release 4: Long Lead Material and Equipment Q3-Q4 2018





Construction Information Sessions*



April 3	Tuesday	Sturtevant
April 4	Wednesday	Platteville
April 6	Friday	Kimberly
April 9	Monday	Madison
April 9	Monday	Janesville
April 10	Tuesday	Racine
April 12	Thursday	Superior
April 13	Friday	Rhinelander
April 16	Monday	Wausau
April 16	Monday	Eau Claire
April 17	Tuesday	Black River Falls
April 17	Tuesday	La Crosse
April 19	Thursday	Pewaukee
April 19	Thursday	Milwaukee

^{*}Schedule and locations as of April 3, 2018 and subject to change





Wisconn Valley Website

Information Resources

Wisconnvalley.wi.gov

Primary site for contractors to engage with public infrastructure and building construction

Wisconnvalley.wi.gov/newsletter

Bi-weekly and breaking news updates on project developments

Wisconnvalley.wi.gov/Pages/General-Info-Sessions.aspx

Details on information sessions throughout the state

Foxconn-construction.gilbaneco.com

Register with M+W|Gilbane to receive automatic bid alerts and information on pre-bid and matchmaking sessions.

In order to ensure a fair and open process, everyone is asked to follow the process.

